

FRACINO PRE-INSTALLATION CHECK SHEET (1)

Dual Fuel Machine Range Only

OFFICE USE:	OUR REF:
-------------	----------


SITE NAME: **TEL:**

SITE ADDRESS:

DEALER NAME (if applicable):

SIGNATURE: **PRINT NAME:**

POSITION IN COMPANY:

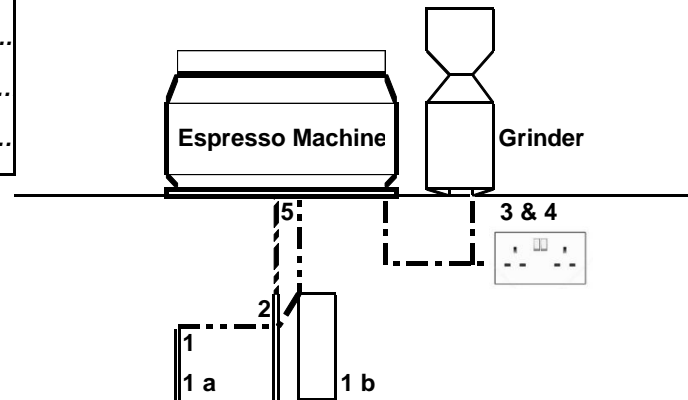

PLEASE NOTE THAT THIS NEEDS TO BE COMPLETED AND RETURNED TO FRACINO A MINIMUM OF 7 WORKING DAYS PRIOR TO REQUIRED INSTALLATION. NO INSTALLATION WILL BE CONFIRMED UNTIL COMPLETED FORM IS RECEIVED. ANY CALLS TO SITE WHERE SERVICES ARE NOT COMPLETE OR CORRECT WILL BE FULLY CHARGEABLE & INSTALLATION ABORTED UNTIL SITE IS PREPARED. PLEASE ENSURE YOU HAVE CUPS AND INGREDIENTS FOR INSTALLATION DATE AND STAFF ARE ON SITE FOR TRAINING. RETURN VISITS ARE CHARGEABLE.

PLEASE CIRCLE 'YES' OR 'NO' BELOW, AS APPLICABLE, TO CONFIRM SERVICES ARE IN PLACE.

1	3/4" B.S.P WASHING MACHINE VALVE FOR MAINS COLD WATER FEED DIRECTLY BENEATH THE COFFEE MACHINE WITHIN 1 METRE	YES / NO
1 a	IF NOT CONNECTING TO MAINS WATER SUPPLY, IS THERE A FLO-JET PUMP OR SIMILAR AND CLEAN WATER TANK PROVIDED?	YES / NO
1 b	HAVE YOU PURCHASED A SUITABLE WATER FILTER/SOFTENER SYSTEM (SUCH AS THE FRACINO DSU SYSTEM)?	YES / NO
2	1.5" (MINIMUM DIAMETER) STAND PIPE OR BUCKET FOR WASTE WATER DIRECTLY BENEATH THE COFFEE MACHINE	YES / NO
3	ESPRESSO MACHINE - 240V 13 AMP MAINS POWER SOCKET (WITHIN 1 METRE & WITH EASY ACCESS TO ISOLATOR)	YES / NO
3 a	IF NOT CONNECTED TO MAINS ELECTRIC SUPPLY, IS A 12V - 240V 1KW INVERTER & 12V BATTERY OR 240V GENERATOR PROVIDED?	YES / NO
4	GRINDER - 240v 13 AMP SOCKET (TO BE ON SAME SIDE AS GRINDER - RECOMMENDED TO BE RIGHT OF MACHINE)	YES / NO
4 a	IF NOT CONNECTED TO MAINS ELECTRIC SUPPLY, IS A 12V - 240V 1KW INVERTER & 12V BATTERY OR 240V GENERATOR PROVIDED?	YES / NO
5	HOLE IN COUNTER: 3" (75mm) DIAMETER (to take both mains water & waste hoses and power cables)	YES / NO
5a	COUNTER TOP IS OF APPROPRIATE FIRE-PROOF MATERIAL & CAN BE DRILLED TO SECURE MACHINE TO FOR MOBILE USE	YES / NO
6	CONFIRM CLEARANCE SPACING AROUND THE MACHINE FOR AIR CIRCULATION (AS SPECIFIED BY FRACINO) IS PROVIDED	YES / NO
6 a	CONFIRM GOOD ACCESS TO ALL SERVICES & MOUNTING POINTS FOR INSTALLATION ENGINEER.	YES / NO
7	SUPPLY PHOTO EVIDENCE OF FIT-OUT, POWER SUPPLY, WATER SUPPLY AND WASTE FOR THE MACHINE TO BE CONNECTED TO	YES / NO
8	CONFIRM COMCAT2 GAS ENGINEER IS ARRANGED TO CERTIFY YOUR INSTALLATION AT TIME OF COMPLETION	YES / NO
9	CONFIRM CUPS, COFFEE (1KG BEANS OR PODS AS RELEVANT) AND MILK ARE TO BE AVAILABLE ON ARRIVAL.	YES / NO
9 a	IF WE AREN'T SUPPLYING THEM, CONFIRM YOU HAVE A COMMERCIAL GRINDER & BARISTA ACCESSORIES WILL BE PROVIDED	YES / NO

IF IN DOUBT ABOUT ANY OF THE ABOVE REQUIREMENTS, PLEASE ASK OUR SUPPORT TEAM FOR ADVICE.

TEL: 0121 328 5757 EMAIL: SALES@FRACINO.COM


RETURN COMPLETED FORM TO: SALES@FRACINO.COM



INSTALLATION PLAN

DUAL FUEL COFFEE MACHINES

PLAN VIEW FOR DRILLING COUNTER



(I) DEPTH FROM BACK OF MACHINE TO HOLE


(II) LENGTH FROM SIDE OF MACHINE TO HOLE

WORK OUT LOCATION OF COFFEE MACHINE ON BAR COUNTER AND MEASURE ACCORDINGLY. HOSES FEED FROM CENTRE OF COFFEE MACHINE THROUGH DRILLED COUNTER

(SEE DIAGRAM OPPOSITE).

1 GROUP	I :	110MM	II :	235MM
2 GROUP	I :	110MM	II :	300MM

1	WATER SUPPLY - MAINS OR FLOJET PUMP
2	1.5" (MINIMUM DIAMETER) STAND PIPE FOR WASTE
3	POWER CONNECTION FOR COFFEE MACHINE
4	WATER SOFTENER (DSU) IF REQUIRED
5	GRINDER - 13 AMP SOCKET REQUIRED
6	ESPRESSO MACHINE
7	HOLE IN COUNTER: 3" (75mm) DIAMETER
8	LPG SUPPLY WITH PRESSURE REGULATOR

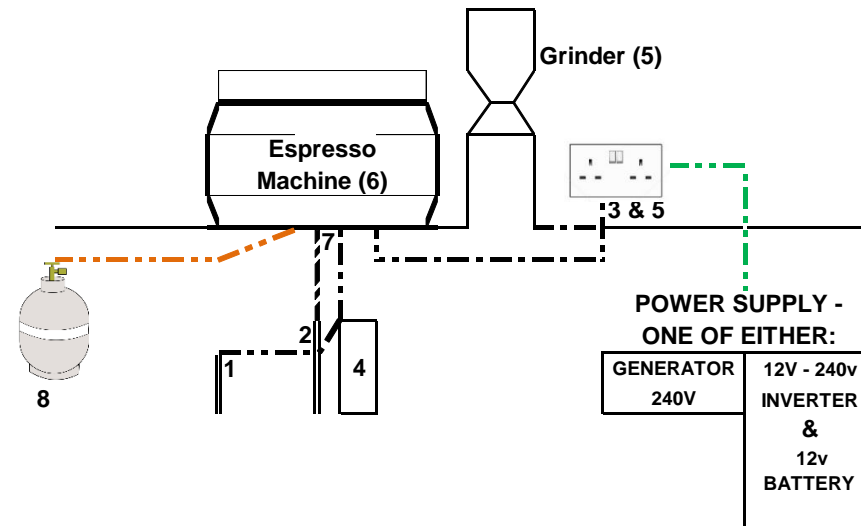

POWER CONNECTIONS WITHIN 1 METRE BEHIND OR BELOW THE MACHINE - WITH EASY ACCESS TO THE ISOLATOR SWITCH

(See Fracino Dual Fuel product brochure for power requirement for your model)

WATER & WASTE CONNECTIONS DIRECTLY BENEATH THE MACHINE

ALL SERVICES, INCLUDING HOLE IN BAR COUNTER MUST BE IN PLACE PRIOR TO ENGINEER BEGINNING THE INSTALLATION.

IF YOU HAVE ANY QUERIES PLEASE CONTACT



SALES@FRACINO.COM

0121 328 5757
